

The Brazos Valley Connection, a 58.7 mile electric transmission line that will run from Harris County to Grimes County, will help address much needed future infrastructure improvements while meeting an obligation to provide safe and reliable power.

Overview as of Feb. 10, 2017

- PUC issued final order April 2016
 - ERCOT target completion: June 2018
 - Construction contractor: North Houston Pole Line
 - Construction start dates:
 - Section K3: 2/6/17*
 - Sections 1, 2, 3: 4/3/17**
- *K3 includes rebuilding approx. 1 mile of an existing tie-line (L.E. Myers Co.)
- **Simultaneous construction of all 3 sections

Section 3


91 tangent poles
42 angle poles
1 lattice angle tower
102,000 double-circuit feet of conductor

Section 2

118 tangent poles
99,500 double-circuit feet of conductor
K3 includes 11 poles and approx. 1 mile of double-circuit conductor

Section 1

125 tangent poles
18 angle poles
2 lattice angle towers
114,000 double-circuit feet of conductor

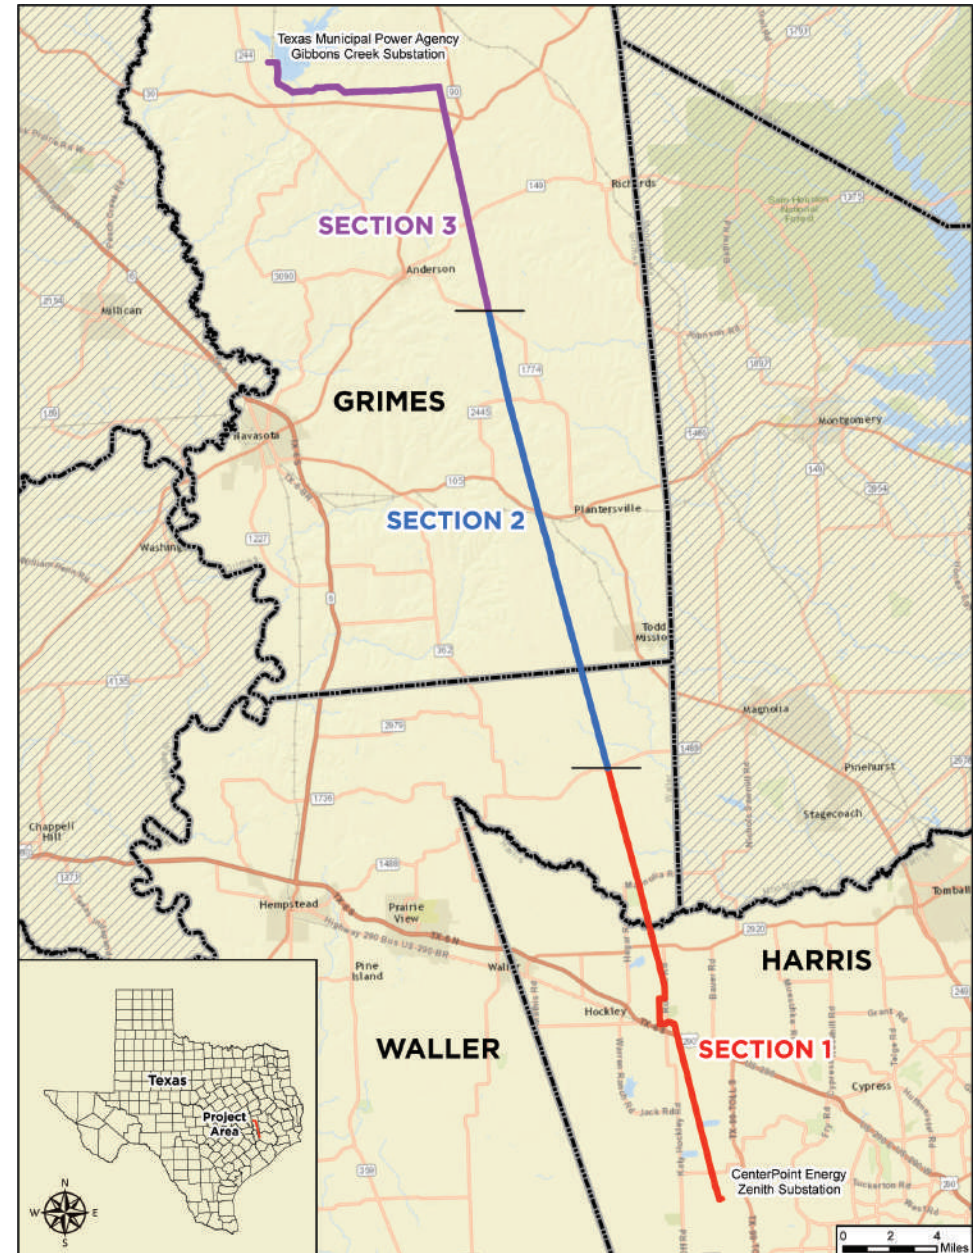



Monopoles are being used throughout majority of project. These are in Section K3 where approximately 1 mile of an existing tie-line is being rebuilt.
